

Riverbanks Zoo and Garden

Phase I, Gift Shop, Guest Services and
Grizzly/Otter Exhibit

Phase II, Seals and Sea Lions



RIVERBANKS ZOO AND GARDEN

ENTRY PLAZA AND EXHIBITS:
GIFT SHOP, GUEST SERVICES, AND GRIZZLY & OTTER EXHIBIT

View of the Guest Services Building from the Northeast



View of the Guest Services Building from the Southeast



Main Entrance Gate Nearly Complete



View of the Gift Shop Building from the Southwest



Entrance Plaza Owner Landscaping and Fencing Nearly Completed



View of the Otter Exhibit Shelter from the South



View of the Otter Exhibit Shelter from the South



Interior of the Otter Viewing Shelter with Ecos Signage



Interior of the Otter Viewing Shelter with Ecos Signage



View from Inside of the Otter Exhibit




View from Inside of the Otter Exhibit



View of the Grizzly Life Support Cave and Softscape




View of the Grizzly Viewing Cave with Ecos Signage

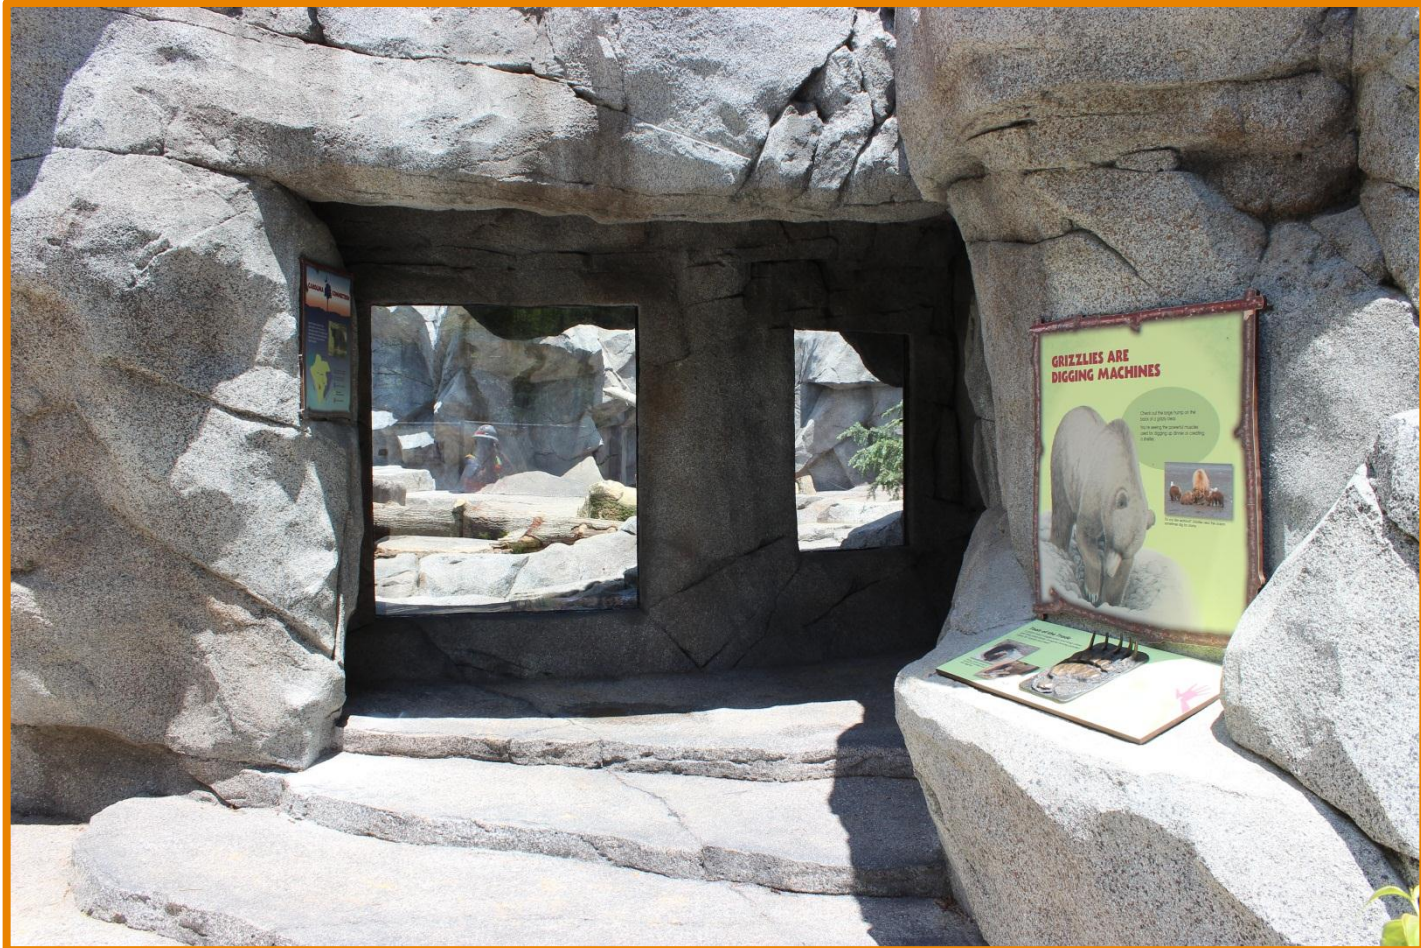

Interior of the Grizzly Viewing Shelter and Ecos Signage



View from Inside the Grizzly Bear Exhibit

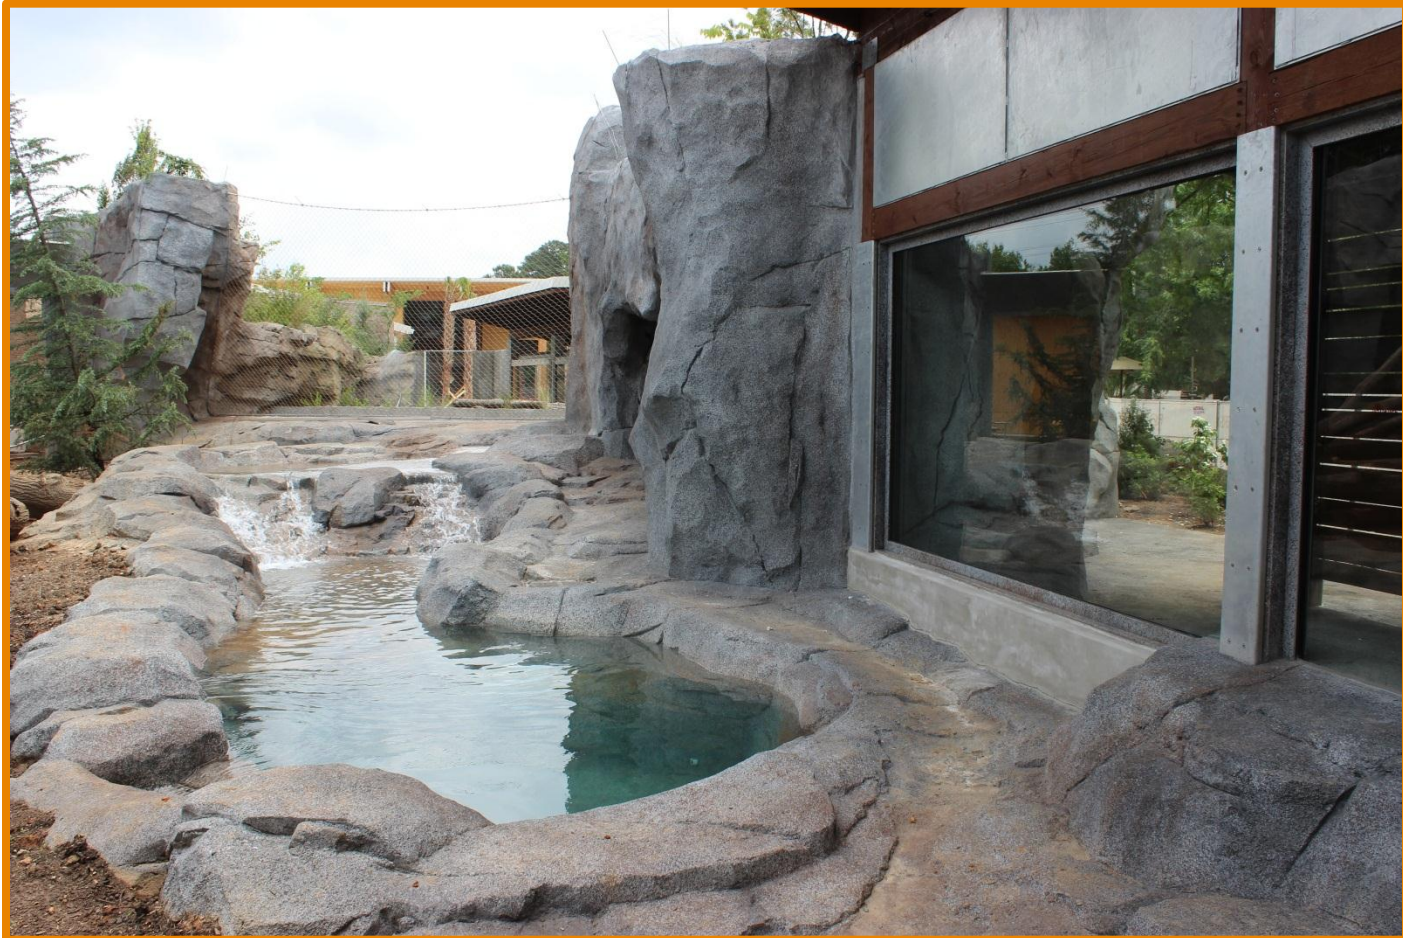

View of the Exhibit Shelter from Inside of Grizzly Bear



View of the Stream and Shelter from Inside of Grizzly



View of the Otter Exhibit from Above



View of the Grizzly Bear Exhibit from Above



SSL LSS Equipment and Platform Installation Progresses



Backfill of the LSS Piping at the Exhibit Pool Progressing



Phase II, CIP Walls Completed Around SSL Exhibit Pool



Grading, Backfilling and Waterproofing for the Viewing Building Progress



Cast In Place Wall Placed at The SSL Holding Building, Ready to Strip



Underslab Utilities Underway at the Holding Building



CMU Walls for Phase II, Holding Building Underway



One Week Look Ahead

The Entrance Gate Structure and Plaza to be completed next week with the placement of the Ticket Tacking Stations and final Electrical trim out. Owner Architect and Engineering Punches are scheduled next week for the Front Gate. Fencing to be completed for Phase I, next week as well as the asphalt paving. Structural Steel to begin for the Viewing Building in Phase II. Final backfill for the Holding Building to be completed along with the Underslab utilities; in preparation for slab on grade placement the following week.



