

Riverbanks Zoo and Garden

Gift Shop, Guest Services and Grizzly/Otter Exhibit



RIVERBANKS ZOO AND GARDEN

ENTRY PLAZA AND EXHIBITS:
GIFT SHOP, GUEST SERVICES, AND GRIZZLY & OTTER EXHIBIT

HARDI Siding Installed at Restroom Building



Construction at the Guest Services Building Progresses



Subgrades at the Guest Services Building being Adjusted



Interior Framing Continues at the Guest Services Building



In-Wall and Overhead Rough Progresses at Guest Services



Framing Nears Completion at the Otter Viewing Shelter Roof



Construction Continues at the Otter Exhibit



Shotcrete Progresses at the Grizzly Bear Exhibit Viewing Cave



Steady Progress being made at the Gift Shop Building




Timber Framing Nearly Complete for the Gift Shop



Split Faced Veneer and Roof Insulation Progresses at Gift Shop LSS



Split Faced Veneer Completed on South Side of LSS Building

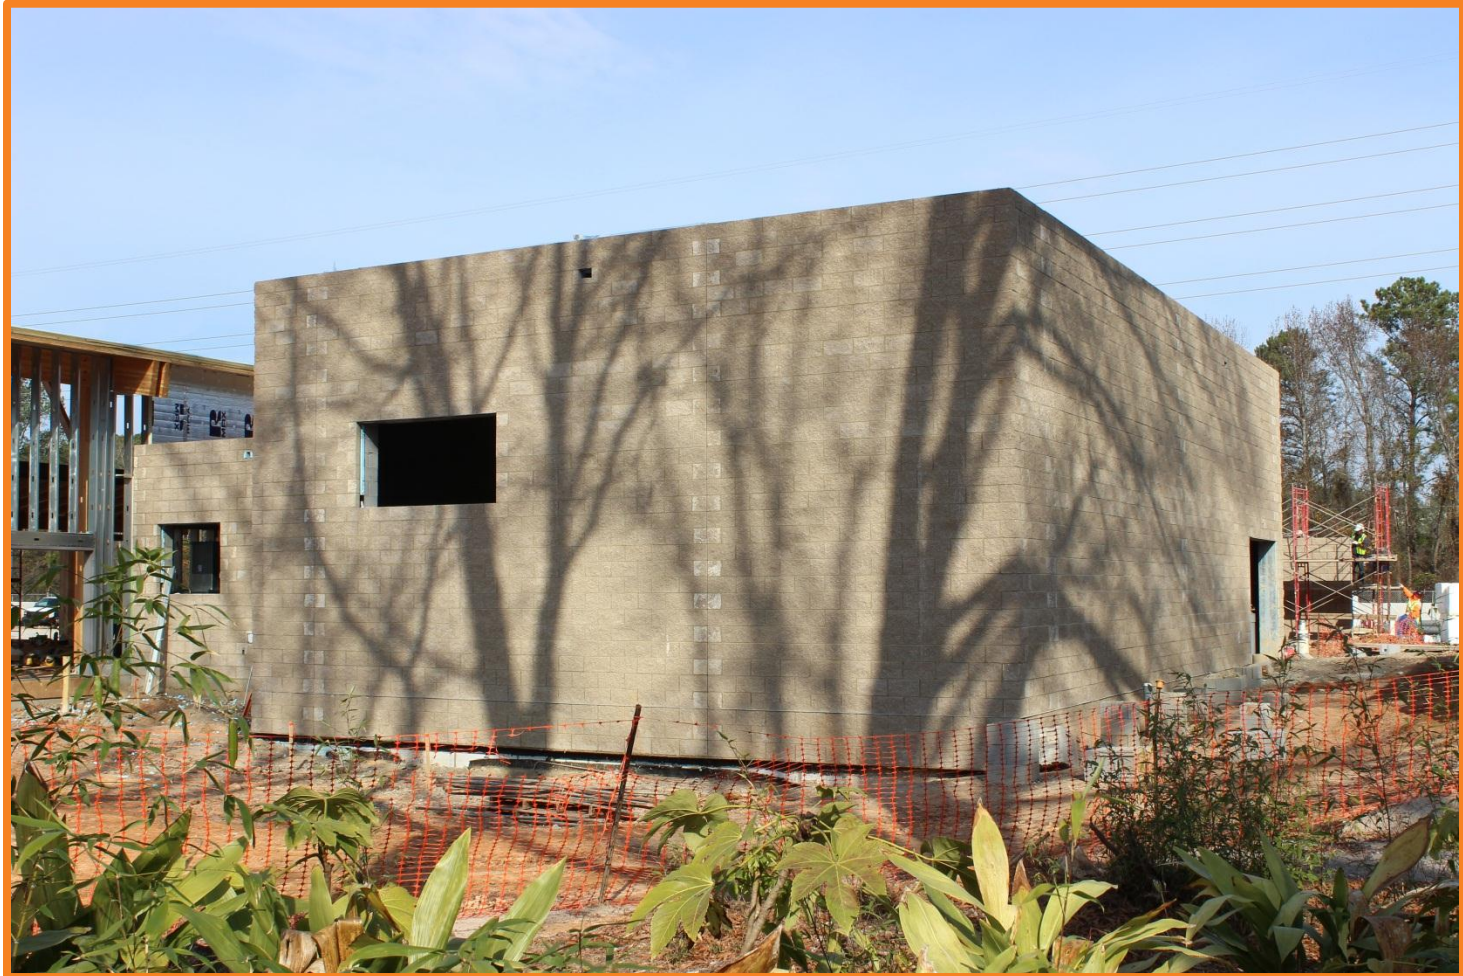

Metal Stud Framing Continues at the Gift Shop



View of the Gift Shop and LSS Building from the Southwest



View of Guest Services and Otter Holding from the Southeast



View of the Otter and Grizzly Exhibits from the Southeast



View of Phase II, Site from the West



View of Phase II Site from the Northeast



View of Phase II Site from the Southeast



New Access Road and Lay Down Area Placed for Phase II



One Week Look Ahead



Exhibit Rock Work to continue next week for both the Otter and Grizzly Bear; with the Grizzly LSS and Viewing Caves taking shape. Overhead and In-Wall rough in to be completed at the Guest Services Building for Mechanical, Electrical, Fire Alarm and Plumbing. Storefront Glass to be measured at both Guest Services and Gift Shop Buildings. Louvers to be installed at the Gift Shop / LSS Building. Subgrade and Layout confirmation of Foundations for Phase II scheduled for next week, in preparation for Rebar and Concrete.



Our Passion is Building®

