

Riverbanks Zoo and Garden


Phase II, Seals and Sea Lions



RIVERBANKS ZOO AND GARDEN

PHASE II, SEALS AND SEA LION EXHIBIT:
EXHIBIT POOL, VIEWING & HOLDING BUILDINGS

Perspective of the Stadium Seating at the North End Of the Exhibit

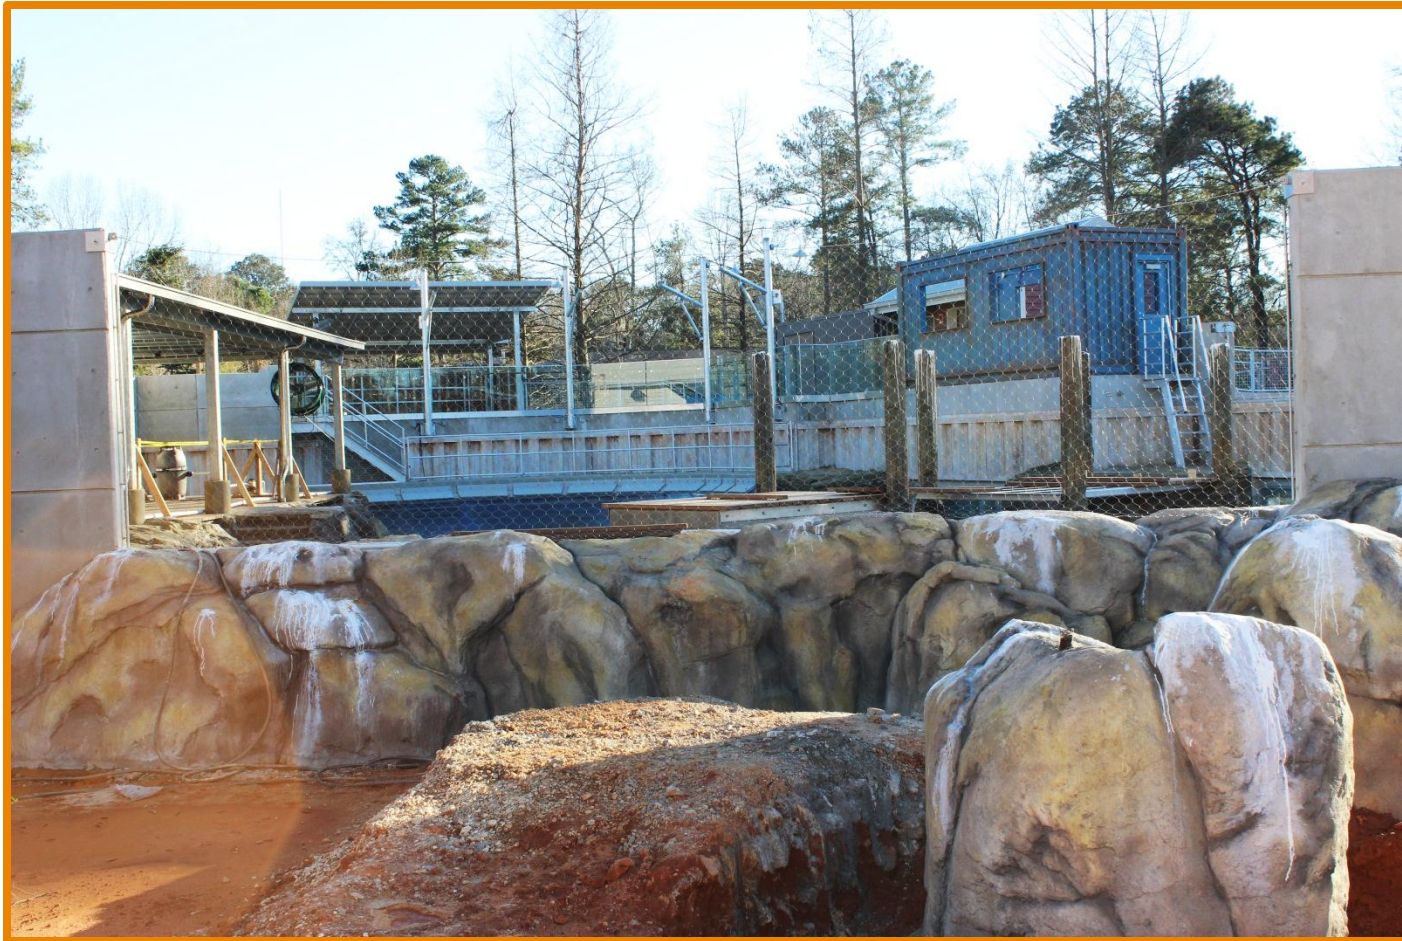

Perspective of the West Entrance to the Viewing Building



Finishes Within the Viewing Building Completed



Flooring Installation Completed for the Viewing Building



Perspective of the Southwest Corner of the Viewing Building



New Hard and Softscape completed behind the Viewing Building



Perspective of the South Entrance to the Viewing Building



Softscape complete between the Holding and Viewing Buildings



Eastern Perspective of the Holding Building



View of the Holding Building from the Upper Viewing Deck



Final Finishes Around the Exhibit Pool Underway



A large, modern, circular water feature, possibly a splash pad or a small pool, with a blue interior. It is surrounded by a wooden deck and a blue building with a white roof. The water is clear and blue, and the surrounding area is landscaped with trees and a clear sky.

Aluminum Ships Ladder Installed at the Shipping Container



View of the Exhibit Pool from the Holding Building Swim Deck



Placement of the Concrete Apron Above the Underground Tanks



Riverbanks Zoo and Garden

Phase III, Pedestrian Bridge



RIVERBANKS ZOO AND GARDEN

PHASE III, PEDESTRIAN BRIDGE PROJECT

Construction Fencing in place to begin Phase III next week



Construction Fencing in place to begin Phase III, next week



One Week Look Ahead

Rodgers Punch List is being worked off next week for the interiors of both buildings in Phase II. The Fabric Shade System is due to arrive next week to cover the Stadium Seating and Shipping Container at the Upper Viewing Deck. The remainder of the IPE wood trim, handrails and decking for the swim platform docks to be installed next week. With the ladders installed this week, the wire mesh barriers are to be installed next week around the Exhibit Pool. The final tie in of the controls for the Wetlands to be completed next week, along with the remainder of the Site Lighting. With the concrete apron placed above the underground tanks outside of the LSS Building, the remainder of the Site Hard and Softscape may resume. Clearing is set to begin on the next Phase of the Riverbanks Zoo Project for the New Pedestrian Bridge; which will tie into the recently completed Main Entrance, Gift Shop and Guest Services Plaza.



YOUR NEW SEAL AND SEA LION EXHIBIT COMING SOON

Our Passion is Building®

