

Riverbanks Zoo and Garden

Gift Shop, Guest Services and Grizzly/Otter Exhibit



RIVERBANKS ZOO AND GARDEN

ENTRY PLAZA AND EXHIBITS:
GIFT SHOP, GUEST SERVICES, AND GRIZZLY & OTTER EXHIBIT

View of the Restroom Building from the Northeast



Subgrade and Compaction Prior to Hardscaping Behind Otter Holding



View of the Guest Services Building from the Northeast



View of the Guest Services Building from the Southeast



Interior Finishes Continue at The Guest Services Building



Otter LSS Equipment Installed and Commissioning Completed



Otter Holding and Keeper Prep Completed



View of the Guest Services Building from the South



View of the Guest Services Building from Above



View of the Otter Exhibit Shelter from the East



View of the Grizzly Life Support Cave and Softscape




Patron's Perspective of the Grizzly Viewing Cave



View of the Grizzly Exhibit Shelter from the West



View from Inside the Grizzly Bear Exhibit

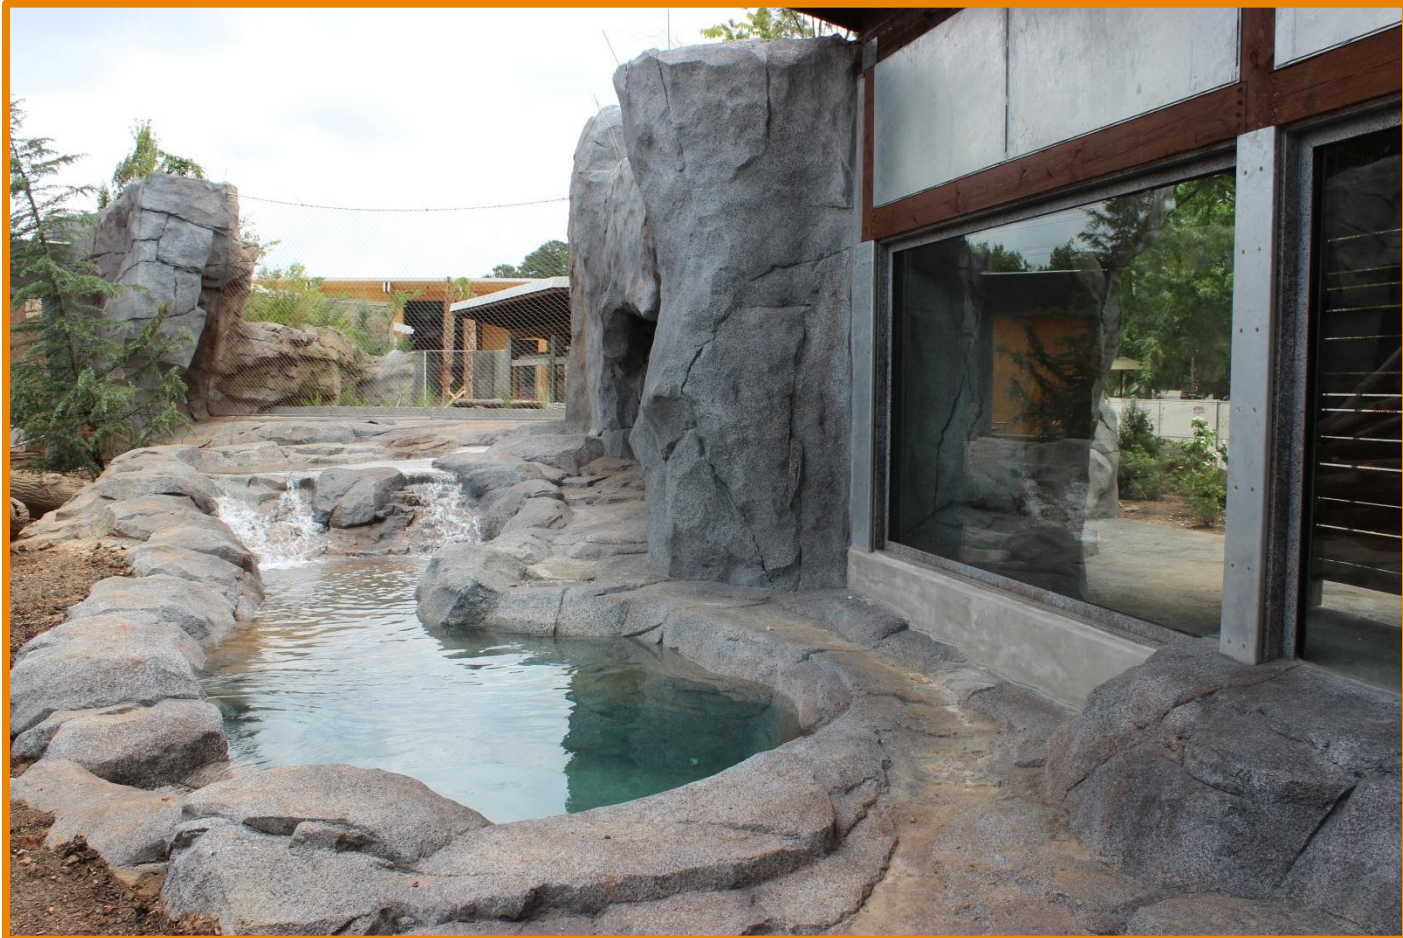

View of the Exhibit Shelter from Inside of Grizzly Bear



View of the Stream and Shelter from Inside of Grizzly



View from Inside of the Otter Exhibit



View from Inside of the Otter Exhibit



View from Inside of the Exhibit Shelter of Otter



View of the Otter Exhibit from Above



View of the Grizzly Bear Exhibit from Above



View of the Otter Exhibit Shelter from the Southeast



Entry Gate Steel Begins Between Guest Services and Gift Shop



View of the Gift Shop from the Southwest



View of the Gift Shop Building from Above



Lighting Installation at the Gift Shop Building



Finishes Progressing for the Ancillary Gift Shop Rooms



View of the Gift Shop Building from the South



View of the SSL LSS Building Behind the Gift Shop



SSL LSS Equipment Installation Continues



Large SSL Pumps Being Assembled Inside the LSS Room



Protein Fractionator Installation Underway



Temporary Road Between the Existing Bird and LSS Buildings



Phase II, LSS Piping Installation Progresses Around the Exhibit Pool



CIP Foundations and Walls Being Placed Around the Exhibit Pool



Underground Branch Electrical Installation at the Viewing Building



View of Phase II, from the West




One Week Look Ahead

With Commissioning completed for the Grizzly and Otter Life Support Systems; punch work continues, as the final touches are made in preparation for the introduction of the Animals next week. Interior Finishes continue for the Guest Services and Gift Shop Buildings in preparation for the Architect and Owner Punch Lists next week. Erection of the Entry Gate Structure to continue next week with the completion of the Structural Steel, followed closely by the wood decking and Coiling Gate installations. Phase II, slab on grade preparations are to begin for the Viewing Building with Underground work completed. The LSS and Plumbing to continue around the Exhibit Pool and Holding Building ahead of concrete placement, backfill and waterproofing.



YOUR NEW GRIZZLY AND OTTER EXHIBITS COMING SOON

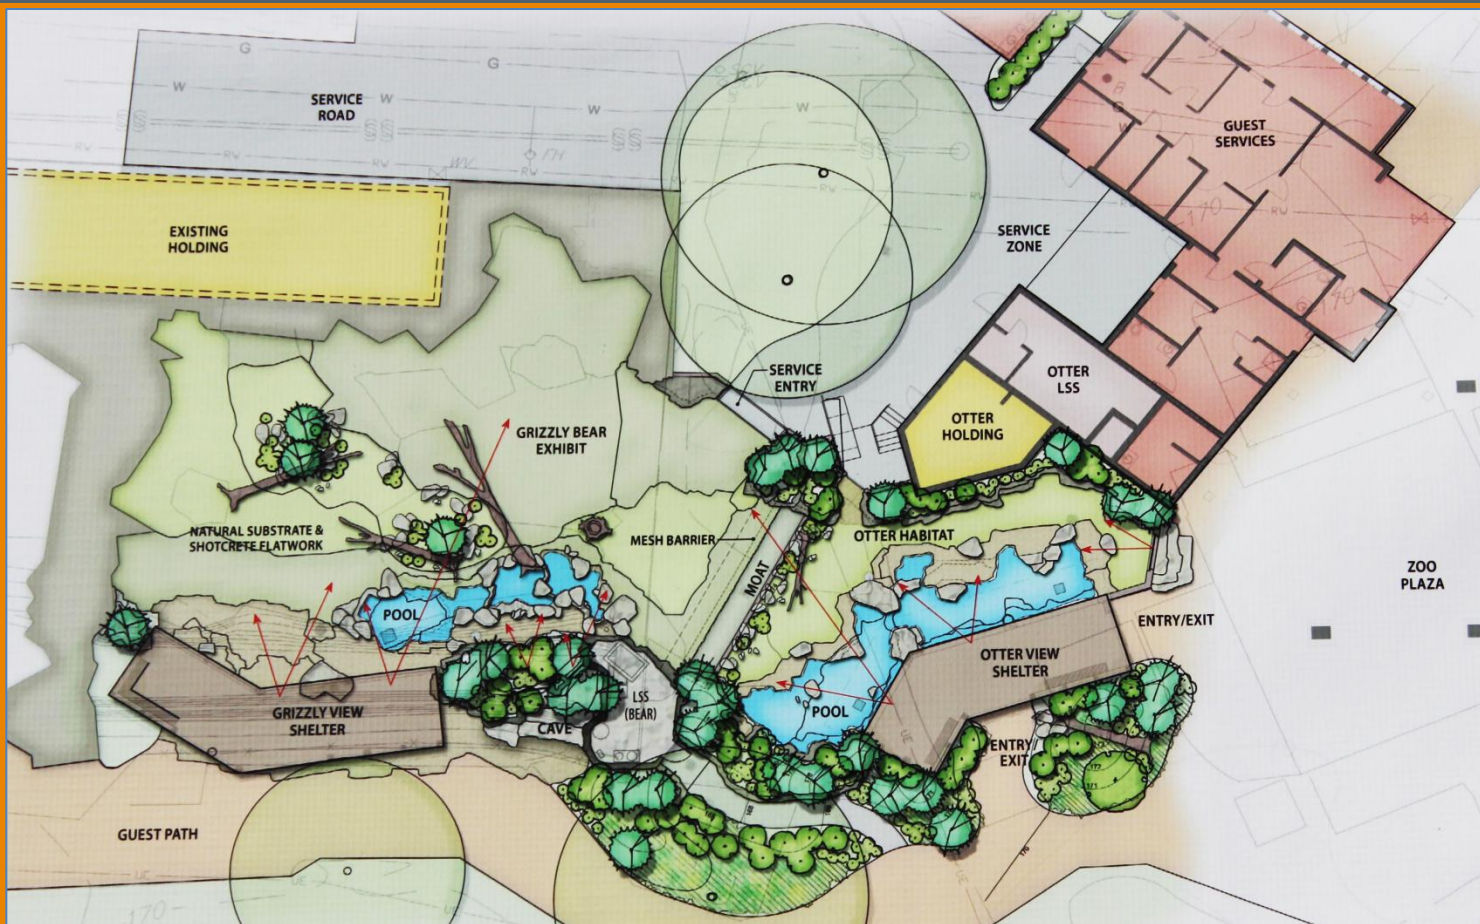

Our Passion is Building®
