

Riverbanks Zoo and Garden

RODGERS

**RIVERBANKS
ZOO & GARDEN**
columbia south carolina

Gift Shop, Guest Services and Grizzly/Otter Exhibit



RIVERBANKS ZOO AND GARDEN

ENTRY PLAZA AND EXHIBITS:
GIFT SHOP, GUEST SERVICES, AND GRIZZLY & OTTER EXHIBIT

05.25-05.29

2015

Our Passion is Building®

View of the Restroom Building from the Northeast



Restroom Building Ready For Final Architectural Inspection



Hardscaping Behind Otter Holding Changed from Asphalt to Concrete



View of the Guest Services Building from the Northeast



View of the Guest Services Building from the Southeast



Main Entrance Gate Continues to Take Shape



Interior Finishes Complete at The Guest Services Building



Interior Finishes Continue at The Guest Services Building



Otter LSS Equipment Installed and Commissioning Completed



View of the Gift Shop Building from the Southwest



Interior of the Gift Shop Building



View of the New Entrance Plaza From Inside of the Zoo




View of the Otter Exhibit Shelter from the South



View of the Grizzly Life Support Cave and Softscape



View of the Grizzly Viewing Cave with Ecos Signage

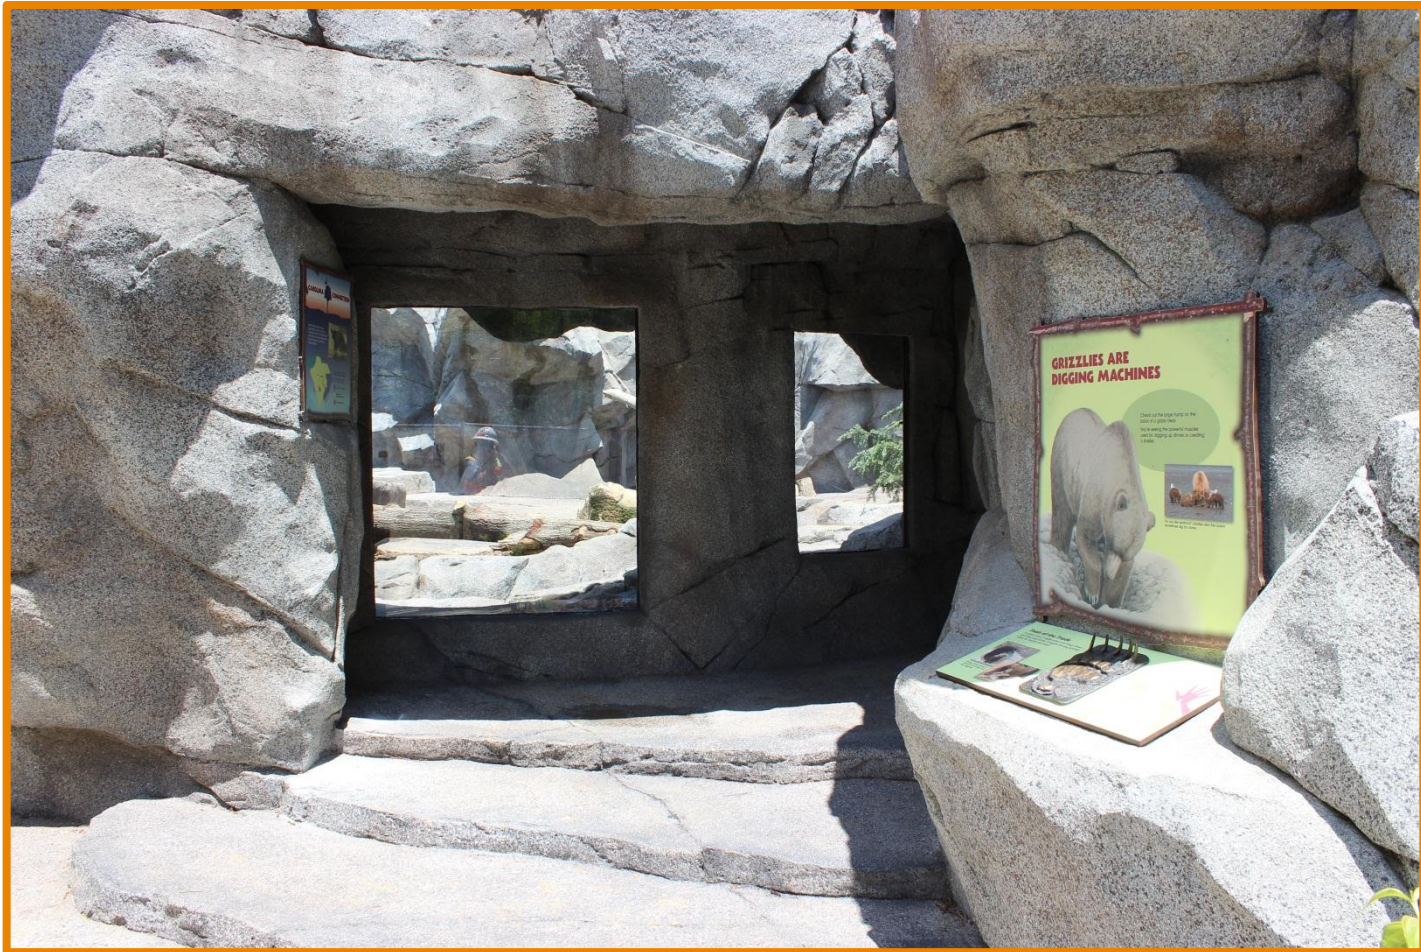


Interior of the Otter Viewing Shelter with Ecos Signage



Interior of the Grizzly Viewing Shelter and Ecos Signage



View from Inside the Grizzly Bear Exhibit

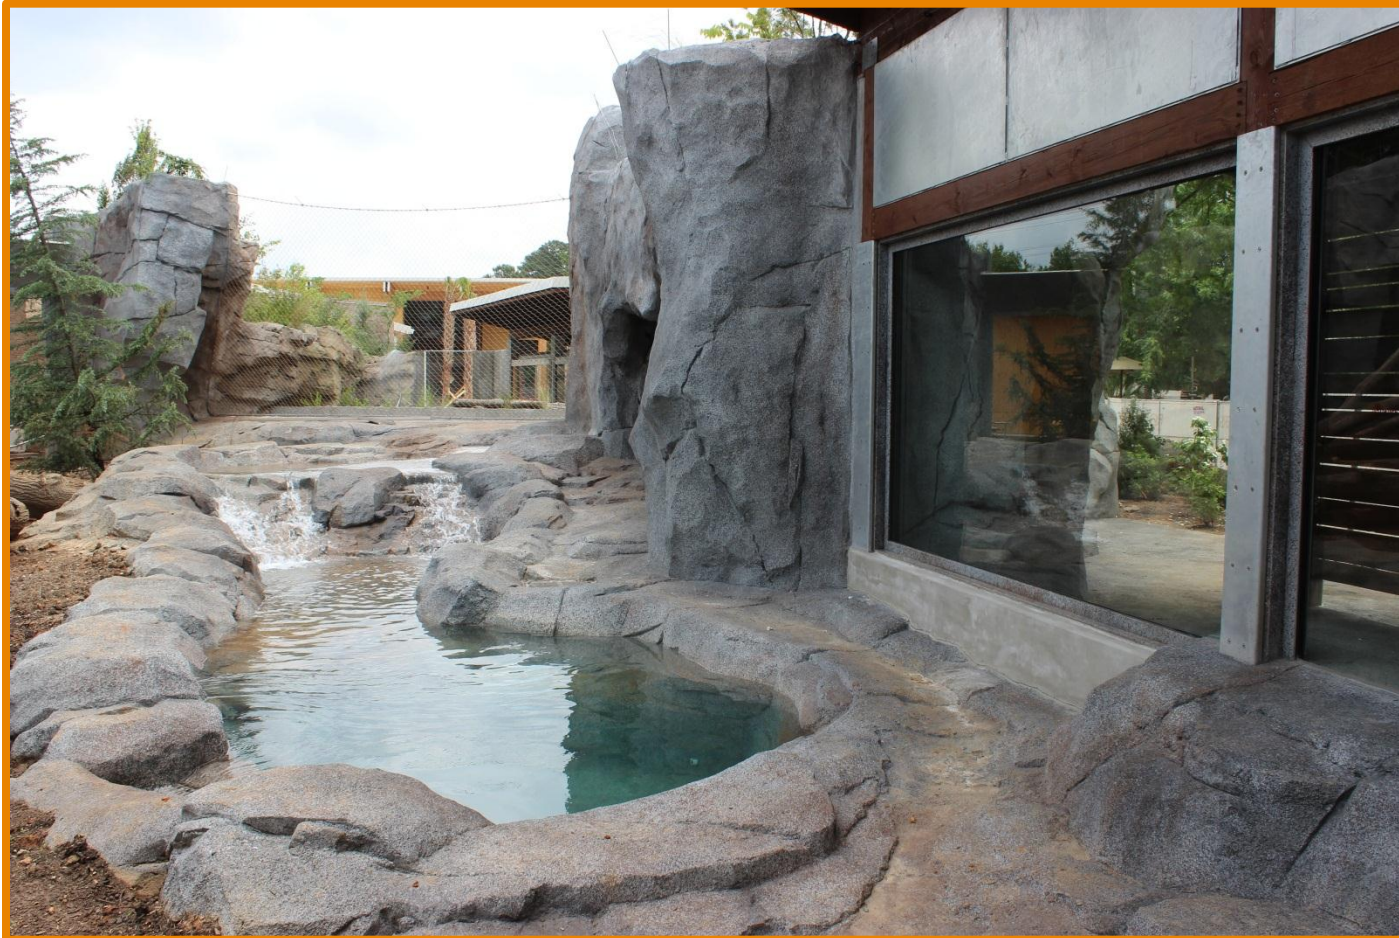

View of the Exhibit Shelter from Inside of Grizzly Bear



View of the Stream and Shelter from Inside of Grizzly



View from Inside of the Otter Exhibit



View from Inside of the Otter Exhibit



View of the Otter Exhibit from Above



View of the Grizzly Bear Exhibit from Above



Chillers Delivered and Equipment Pads Placed at SSL LSS



SSL LSS Equipment Installation Continues



Large SSL Pumps Being Assembled Inside the LSS Room



Protein Fractionator Installation Underway



Phase II, Exhibit CIP Walls and LSS Underground Piping Progress



Holding Building CIP Wall Placement Underway




CMU Walls for Phase II, Holding Building Underway



One Week Look Ahead

Final Architectural and Engineering Punch Lists have been developed for Phase I, Buildings: Restroom, Guest Services, Gift Shop and Exhibits; with those items to be completed by the end of next week. Hardscaping around Phase I, Buildings to continue to progress next week; as the Entry Gate Structure takes shape. The Otters have been acclimating to their new environment this week, with the Grizzly Bears arriving this weekend. Completion of the Foundation Waterproofing and Backfilling of Phase II, Exhibit Walls scheduled for next week. Elevated Slabs and Walls to be placed at the Viewing Building. Structural Steel to be placed the following week at Holding.

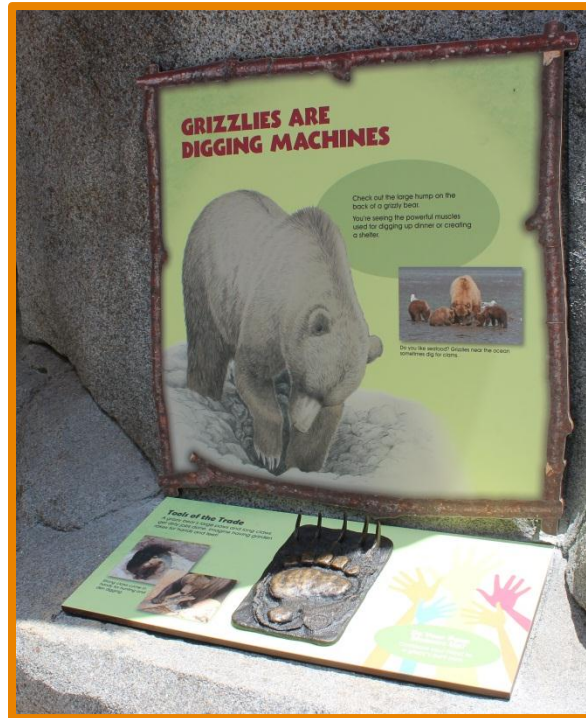

YOUR NEW GRIZZLY AND OTTER EXHIBITS COMING SOON



Our Passion is Building®
