



Riverbanks Zoo and Garden

Phase II, Seals and Sea Lions





RIVERBANKS ZOO AND GARDEN


PHASE II, SEALS AND SEA LION EXHIBIT: EXHIBIT POOL, VIEWING & HOLDING BUILDINGS







Adjustments To The LSS Water Piping To And From The Chillers

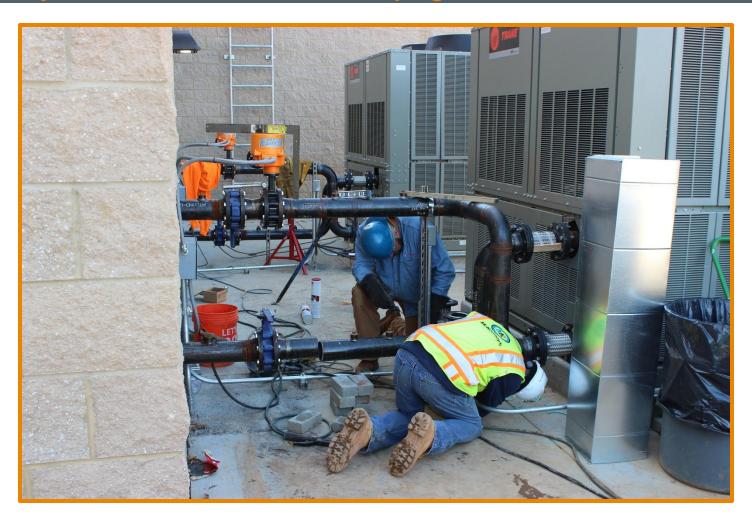







Work Progresses on the SSL LSS Defender Filters and Piping









Work Continues on the SSL LSS Heat Exchangers









The Protein Fractionator Has Been Raised and Re-Piped









Work Continues on the SSL LSS Equipment Pumps and Piping









Work Continues on the SSL LSS Storage Tanks









Perspective of the West Entrance to the Viewing Building









Glass Handrailing Installation At The Lower Viewing Area










Tile Work Continues In Viewing Building As Finishes Progress

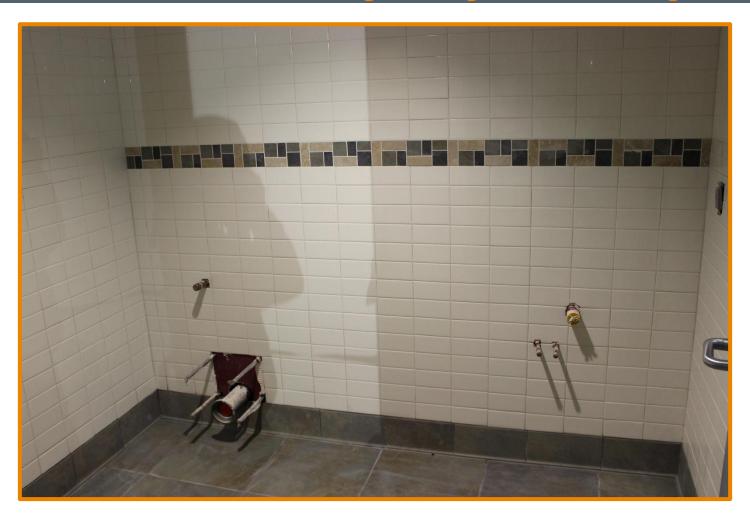







Perspective of the Southwest Corner of the Viewing Building







Perspective of the South Entrance to the Viewing Building







Installation of the Roof Pavers Progress at the Upper Viewing Deck









Backfill Progresses Between the Viewing and Holding Buildings









Work On The Access Road Continues To Progress At Holding









Perspective of the East Side of the Holding Building









Stainless Steel Counters and Plumbing Fixtures Progress at Holding









Siding Is Complete At The Holding Building









Perspective of the Holding Building from Upper Viewing Deck









Rockwork Structural Base Continues To Progress At The Exhibit Pool





One Week Look Ahead

Glass Handrailing Installation to continue at the Viewing Building next week. The Owner to pull Telecommunications and Data Wiring next week, in preparation for Fire Alarm check out immediately following. Installation of Finishes continues at the Holding Building next week with Ceiling Tiles and Fans, Doors and Hardware, and Plumbing Fixtures and trim out. Work continues next week within the Exhibit Pool

with placement of the last sections of the Structural Base Coat of the Exhibit Rockwork. Work scheduled to begin on the Wetlands with tie in of the LSS Piping and Excavation Markers to be set immediately following the Asphalt Paving of the Access Road behind the Holding Building.

Mike Nardella to return for his next Site Visit on Tuesday and Wednesday of next week.







uilding

Our Passion

YOUR NEW SEAL AND SEA LION EXHIBIT COMING SOON











