

# Riverbanks Zoo and Garden

## Phase II, Seals and Sea Lions



## RIVERBANKS ZOO AND GARDEN

PHASE II, SEALS AND SEA LION EXHIBIT:  
EXHIBIT POOL, VIEWING & HOLDING BUILDINGS

12.07-12.11

**2015**



## Grading has Begun for the Stadium Seating





## Perspective of the West Entrance to the Viewing Building





## Perspective of the Southwest Corner of the Viewing Building





## Grading has Begun for the Hardscape to the South Viewing





## Perspective of the South Entrance to the Viewing Building



## Ceilings Inside of the Viewing Building Receive Dry Fall Paint





## Progress at the Upper Viewing Deck Continues





## Landscaping has Begun Between Holding and Viewing





## Landscaping Progresses Behind the Viewing Building





## Caging Installation has Begun at the Holding Building





## Eastern Perspective of the Holding Building





## Northwest Perspective of the Holding Building





## Perspective of the Holding Building from Upper Viewing Deck





## Installation of the Rockwork Caging Begins at the Exhibit Pool






## One Week Look Ahead

**Work on the interior of the Viewing Building to progress next week with the ASI-018 changes continuing, dry fall painting of the ceilings, and installation of the light fixtures next week. The placement of the stadium seating to begin next week at the North Entrance to the Viewing Building. Placement of the hardscape at the South Entrance to the Viewing Building beginning as well.**

**Caging installation continues next week at the Holding Building; along with the installation of the skylight above the Quarantine Pool.**

**Progress for the Exhibit Rockwork continues next week with the placement of the structural support caging and carving of the rockwork formations both in and outside of the Exhibit Pool.**

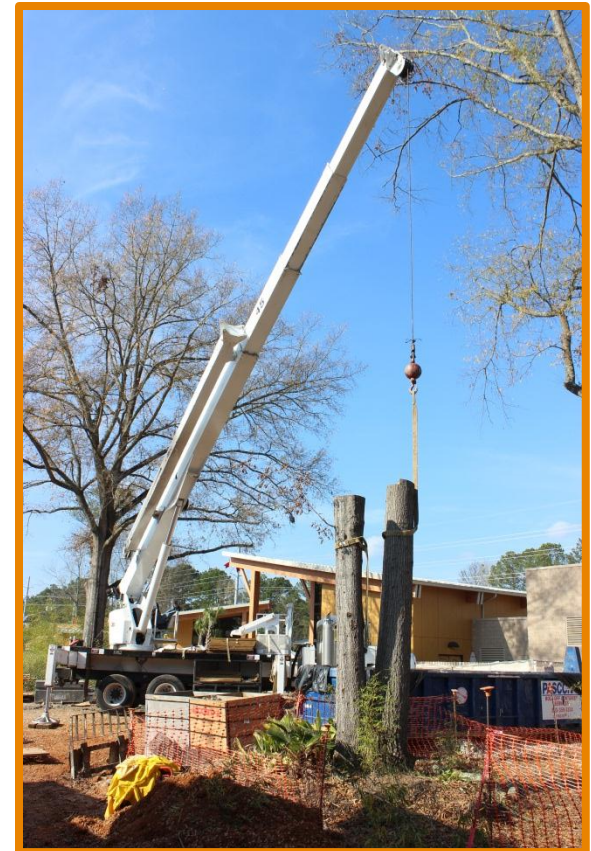



**Our Passion is Building®**

